

Noyes Laboratory (0012)

Classroom Renovation

Building Information

Year Built: 1914

Project Area Primary Users: Students

Affected Rooms: 111, 203, 204, 217, 300, 301, 303, 304


Room Capacities: 111: 40 seats, 203: 40 seats,
204: 45 seats, 217: 101 seats, 300: 30 seats,
301: 30 seats, 303: 30 seats, 304: 40 seats

Narrative

This project upgraded west wing general assignment classrooms, corridors, and ancillary spaces. **New windows & exterior doors, HVAC, and life safety upgrades** were installed on the west wing of Noyes Laboratory.

Restrooms were also remodeled. Lecture hall **seating** was replaced in Room 217. **Exterior doors** were replaced with energy efficient door systems and **exterior stair systems** upgraded. **Window A/C units** were removed and this area was served with **new AHU units and campus chilled water**. With the addition of campus unit funding, this project could include a comprehensive west wing renovation including offices and departmental space. Interior finishes will be updated as required. **Fin tube radiation** will replace cast iron radiators. **This project will compliment a current exterior envelope repair project.**

The project required a conceptualization or feasibility study to further define scope and budget and to incorporate users' requests and associated funding. It would have been possible for additional adjacent spaces such as offices to be renovated simultaneously if departmental funding was provided.

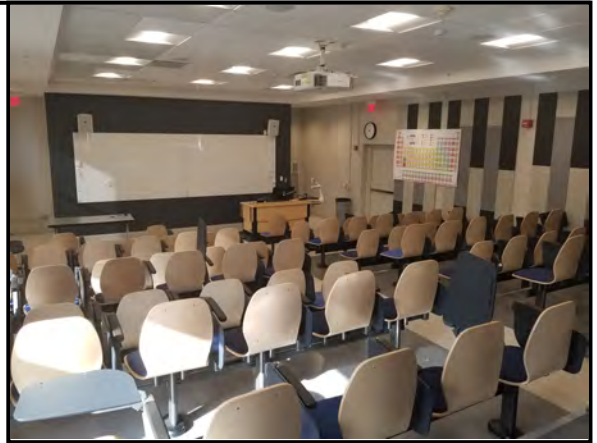

Existing Conditions

After

Room 217 - Left
Updated seating and IT equipment

Room 304 - Right
Renovated windows



Before

Room 217 - Left
Damaged IT equipment

Room 304 - Center
Current Air Conditioning

Room 304 - Right
Antiquated and deteriorated windows

